

6 November 2009

Drilling and Seismic Update WestSide's drilling and appraisal continues

Current activity

- **Tilbrook:** #9a vertical well logged, tested and cased as a future producer.
- **Paranui:** Seismic acquisition completed.

Up to 16 wells are planned as part of the 2009 / 2010 exploration program across WestSide's tenements.

ATP 688P coal seam gas drilling program (Tilbrook)

WestSide continues a multi well program in ATP 688P in the northern Bowen Basin to confirm coal in the P seam and Goonyella seams of the Moranbah Coal Measures in preparation for the drilling of two sets of horizontal chevron-style dual-lateral wells (Tilbrook #L9a and #L9b, Tilbrook #L10a and #L10b) which are planned to intersect with new vertical wells (Tilbrook #9 and #10).

Based on the results of the Tilbrook #9a well it is now planned to drill Tilbrook T9 prior to T10a and T10b to assist in the design of the Tilbrook #L9 lateral set. Tilbrook #9 is planned as a vertical production well.

Latest activity – Tilbrook #9a

The Tilbrook #9a vertical exploration well has been drilled to a depth of 506m, logged, subjected to two drill stem tests and cased. The well shows more than 9 metres of net coal.

Summary : ATP 688P coal seam gas drilling program (Oct – Nov)

Well	Well Type	Spud Date	Finish Date	Current Status
Tilbrook # 9a	Exploration	16 Oct 2009	5 Nov 2009	Drilled to 506m, logged, cased and 2 DST's complete. Suspended as future producer.
Tilbrook # 9 vertical	Exploration	8 Nov 2009 (Planned)	20 Nov 2009 (Planned)	Preparing to drill then shutdown for a planned crew break.
Tilbrook # 10b	Exploration	22 Nov 2009 (Planned)	4 Dec 2009 (Planned)	Site preparation completed.
Tilbrook # 10a	Exploration	6 Dec 2009 (Planned)	12 Dec 2009 (Planned)	Site preparation in progress.

Boart Longyear is the drilling contractor.

Expected operations in the next week

Commence drilling T9. Site preparations will continue at Tilbrook #10a.

ATP 688P and ATP769P coal seam gas seismic program (Tilbrook, Mount Saint Martin and Paranui)

WestSide has completed its seismic acquisition program in the Tilbrook and Mount Saint Martin areas of ATP 688P and in Paranui in ATP 769P.

Latest activity

Seismic acquisition over a 10km distance was commenced at Paranui on 3 November and was completed on 4 November.

Summary : Seismic program

Area	Type	Start	Finish Date	Current Status
Mt St Martin (ATP 688P)	5 km of Vibroseis	19 Oct 2009	21 Oct 2009	Completed. Data processing.
Tilbrook (ATP 688P)	5 km of Vibroseis	22 Oct 2009	23 Oct 2009	Completed. Data processing
Paranui (ATP 769P)	10 km of dynamite seismic	3 Nov 2009	4 Nov 2009	Acquisition completed.

Expected operations in the next week

This completes the acquisition of seismic in this program. Data processing and analysis will continue.

About WestSide Corporation Ltd

WestSide Corporation Limited is listed on ASX (ASX code: WCL) and has interests in coal seam gas (CSG) projects in Queensland and Indonesia. WestSide has a 50% interest in ATP 688P and ATP 769P with QGC holding the other 50%.

WestSide is currently operating an appraisal program in ATP 769P (Paranui) and ATP 688P (Tilbrook, Mount Saint Martin and Bald Hill) sites in Queensland's Bowen Basin, and is also assessing the CSG potential of certain coal deposits in Indonesia through its relationship with PT Bumi Resources TBK, one of Indonesia's largest coal miners.

Regular updates will be provided during the course of the drilling campaign.


Additional information is available on WestSide's website: www.westsidecorporation.com.

For further information contact:

WestSide Corporation Ltd
 Angus Karoll
 Chairman and Acting CEO
 07 3020 0900

Media
 Anna O'Gorman
 Principal Consultant - Three Plus
 07 3503 5700
 0423 463 548

Tilbrook CSG Pilot Area

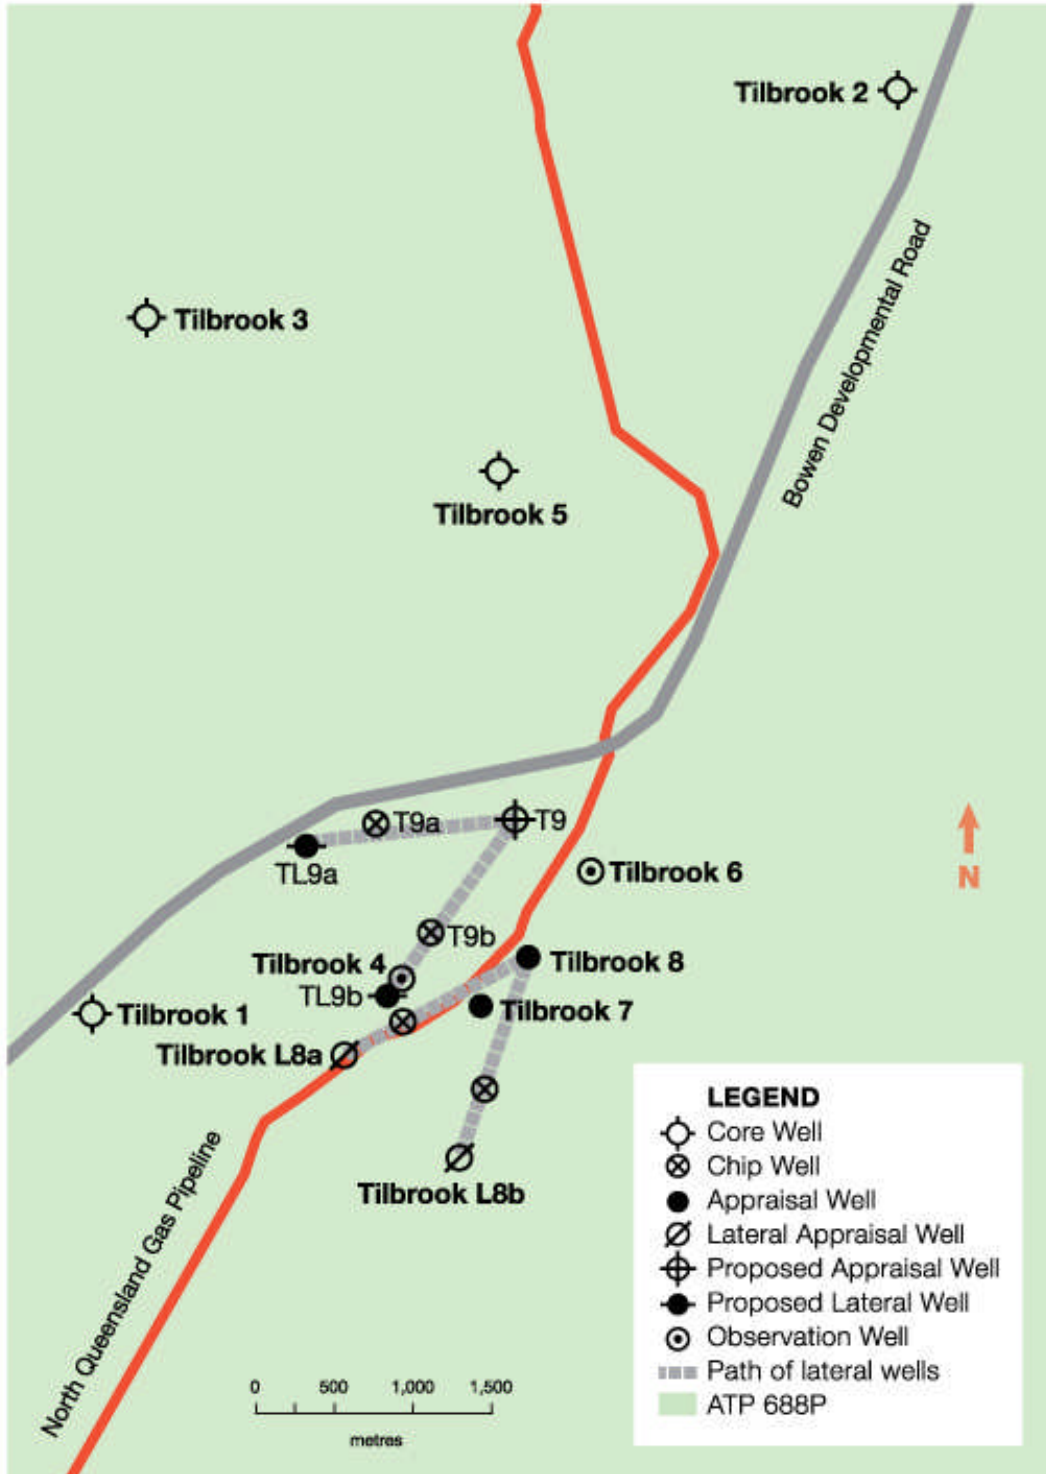

ATP 769P Area of Operations (Paranui)

